


CareerScribe Alpha
Work Plan

ID	Task Name	Duration	Start	Finish	%	Work	Preced	February Feb	March Mar	April Apr	May May	June Jun	July Jul	August Aug	September Sep
1	CareerScribe Alpha Project	92.88 days?	Mon 4/7/08	Wed 8/13/08	65%	1,057 hrs									66%
2	Analysis - Use Case Confirmation	53.25 days	Tue 4/8/08	Fri 6/20/08	100%	107 hrs									
3	Login-Use Case Confirmed	0 days	Tue 4/8/08	Tue 4/8/08	100%	0 hrs									
4	Registration-Use Case Revisions	0 days	Tue 4/8/08	Tue 4/8/08	100%	0 hrs									
5	Alpha Use Cases	5.25 days	Wed 6/11/08	Wed 6/18/08	100%	75 hrs									
6	Messaging-Use Case Confirmed	0.5 days	Wed 6/11/08	Wed 6/11/08	100%	7 hrs									
11	Professional Dashboard--Use Case Revisions	4 hrs	Wed 6/11/08	Wed 6/11/08	100%	4 hrs 10									
12	Employer Profile-Use Case Confirmed	4 hrs	Thu 6/12/08	Thu 6/12/08	100%	8 hrs 11									
13	Employer Dashboard-Use Case Confirmed	4 hrs	Thu 6/12/08	Thu 6/12/08	100%	8 hrs 12									
14	Search-Use Case Confirmed	4 hrs	Fri 6/13/08	Fri 6/13/08	100%	8 hrs 13									
15	Search Results-Use Case Confirmed	4 hrs	Fri 6/13/08	Fri 6/13/08	100%	8 hrs 14									
16	Algorithms-Use Case	4 hrs	Mon 6/16/08	Mon 6/16/08	100%	8 hrs 15									
17	Company Job Management-Use Case Confirmed	4 hrs	Mon 6/16/08	Mon 6/16/08	100%	8 hrs 16									
18	Company Saved Candidates	4 hrs	Tue 6/17/08	Tue 6/17/08	100%	8 hrs 17									
19	Candidate Saved Jobs	4 hrs	Tue 6/17/08	Tue 6/17/08	100%	8 hrs 18									
20	Develop Video Use Case (create from prototype)	0 hrs	Wed 6/18/08	Wed 6/18/08	100%	0 hrs 19									
21	Develop Requirements Workbook(Use Case Confirmation)	2 days	Wed 6/18/08	Fri 6/20/08	100%	32 hrs 20									
22	Design	16 days?	Thu 6/12/08	Fri 7/4/08	75%	128 hrs									
26	Construction	66.88 days?	Mon 4/7/08	Tue 7/8/08	95%	494 hrs									
27	Completed Code Components	14.25 days?	Mon 4/7/08	Fri 4/25/08	100%	110 hrs									
46	Messaging	56 days	Mon 4/7/08	Mon 6/23/08	100%	66 hrs									
47	Inbox / Sent Items	1 day	Wed 6/18/08	Wed 6/18/08	100%	4 hrs									
48	Messages / Conversation Sorted by Date	1 day	Wed 6/18/08	Wed 6/18/08	100%	4 hrs									
49	Select Messages	1 day	Thu 6/19/08	Thu 6/19/08	100%	8 hrs 48									
50	Compose Messages	2 days	Fri 6/20/08	Mon 6/23/08	100%	16 hrs									
51	My Contacts	2 days	Fri 6/20/08	Mon 6/23/08	100%	16 hrs 48									
52	View Message	3 days	Thu 6/19/08	Mon 6/23/08	100%	10 hrs									
53	Conversation View	1 day	Thu 6/19/08	Thu 6/19/08	100%	4 hrs 48									
54	Reply	1 day	Fri 6/20/08	Fri 6/20/08	100%	4 hrs 53									
55	Video Reply	1 day	Mon 6/23/08	Mon 6/23/08	100%	2 hrs 54									
56	Interview Invitation	1 day	Wed 6/11/08	Thu 6/12/08	100%	8 hrs									
57	Complete Interview Request	0.5 days	Wed 6/11/08	Wed 6/11/08	100%	4 hrs 7									
58	Complete Interview Accept/Decline	0.5 days	Wed 6/11/08	Thu 6/12/08	100%	4 hrs 57									
59	Edit Automated Messages	0.5 days	Thu 6/12/08	Thu 6/12/08	100%	4 hrs 58									
60	End Dialogue	0.5 days	Mon 4/7/08	Thu 6/12/08	100%	4 hrs 58									
61	Candidate Profile Submission	0.5 days	Thu 6/12/08	Thu 6/12/08	100%	4 hrs 58									
62	Company-Candidate Communication	1 day	Wed 6/18/08	Thu 6/19/08	100%	8 hrs									
63	Candidate Profile	51 days	Mon 4/7/08	Tue 6/17/08	100%	36 hrs									
64	Save Candidate to Job by Company	1 day	Thu 6/12/08	Fri 6/13/08	100%	8 hrs									
65	Save to Job or Pipeline	8 hrs	Thu 6/12/08	Fri 6/13/08	100%	8 hrs 59									
66	% Complete of Profile	2 hrs	Mon 4/7/08	Mon 4/7/08	100%	2 hrs 65									
67	Ideal Job	2 hrs	Mon 4/7/08	Mon 4/7/08	100%	2 hrs 66									
68	Job Preferences	4 hrs	Fri 6/13/08	Fri 6/13/08	100%	4 hrs 67									
69	Privacy Settings	4 hrs	Fri 6/13/08	Fri 6/13/08	100%	4 hrs 68									
70	Work Experience	4 hrs	Fri 6/13/08	Mon 6/16/08	100%	4 hrs 69									
71	Education	4 hrs	Fri 6/13/08	Mon 6/16/08	100%	4 hrs 70									
72	Video	4 hrs	Fri 6/13/08	Tue 6/17/08	100%	4 hrs 71									
73	CareerTracker	4 hrs	Fri 6/13/08	Tue 6/17/08	100%	4 hrs 72									
74	Candidate Dashboard	48 days	Tue 4/15/08	Fri 6/20/08	94%	36 hrs									
75	Content Management Areas	8 hrs	Tue 4/15/08	Tue 6/17/08	75%	8 hrs 73									
76	Messages	4 hrs	Fri 4/18/08	Tue 6/17/08	100%	4 hrs 75									
77	Opportunity Knocks	24 hrs	Tue 6/17/08	Fri 6/20/08	100%	24 hrs 76									
78	Company Profile	55 days	Mon 4/7/08	Fri 6/20/08	75%	28 hrs									
79	Welcome Overlay	4 hrs	Fri 6/20/08	Fri 6/20/08	75%	4 hrs									
80	Company Profile	4 hrs	Fri 6/20/08	Fri 6/20/08	75%	4 hrs									
81	Company Information	4 hrs	Mon 4/7/08	Mon 4/7/08	75%	4 hrs									
82	Company Perks	4 hrs	Fri 6/20/08	Fri 6/20/08	75%	4 hrs									
83	Video	4 hrs	Fri 6/20/08	Fri 6/20/08	75%	4 hrs									
84	Company Overview	4 hrs	Fri 6/20/08	Fri 6/20/08	75%	4 hrs									
85	Best Practices Admin	4 hrs	Mon 4/7/08	Mon 4/7/08	75%	4 hrs									
86	Company Dashboard	1.75 days	Fri 6/20/08	Tue 6/24/08	75%	14 hrs									
87	Current Features	14 hrs	Fri 6/20/08	Tue 6/24/08	75%	14 hrs									
88	Position Maintenance	3.25 days	Fri 6/20/08	Wed 6/25/08	100%	8 hrs									
89	Edit / Delete a Position	1 day	Fri 6/20/08	Wed 6/25/08	100%	8 hrs									
90	Search	6 days	Mon 6/23/08	Tue 7/1/08	100%	48 hrs									

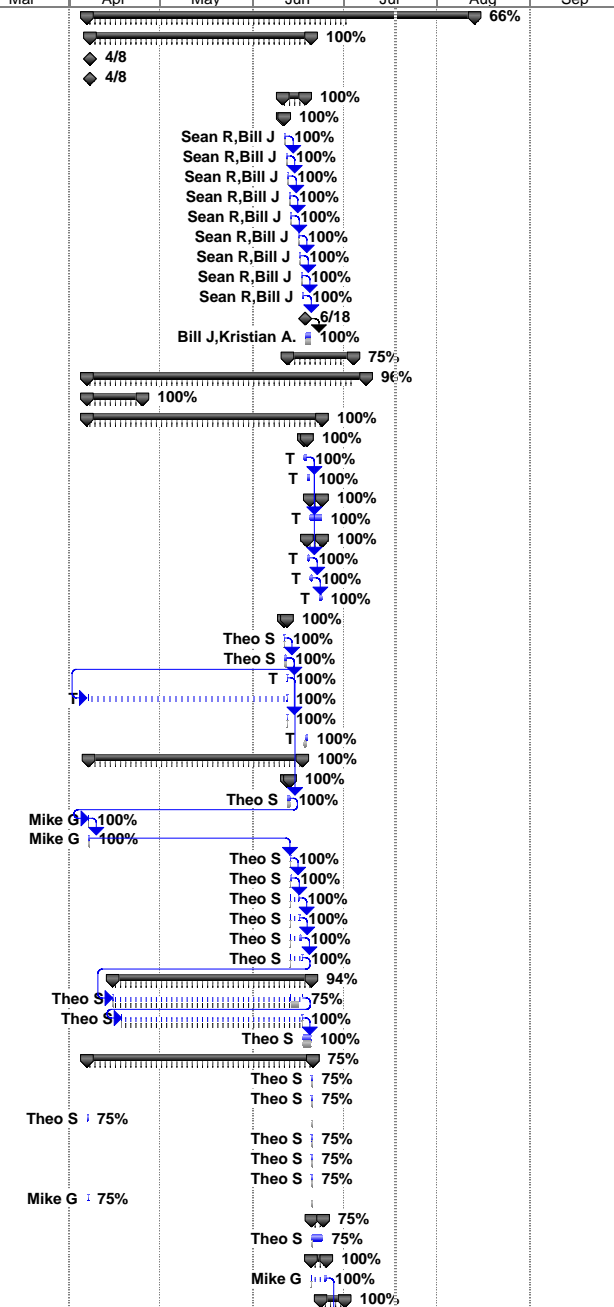

CareerScribe Alpha
Work Plan

ID	Task Name	Duration	Start	Finish	%	Work	Preced	February	March	April	May	June	July	August	September
								Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
91	Complete Advanced Search - Candidate	3 days	Mon 6/23/08	Fri 6/27/08	100%	24 hrs	89								
92	Complete Advanced Search - Company	3 days	Thu 6/26/08	Tue 7/1/08	100%	24 hrs	91								
93	Search Results	5.25 days	Tue 7/1/08	Tue 7/8/08	86%	42 hrs									
94	Candidate Search Results	2.25 days	Tue 7/1/08	Thu 7/3/08	100%	18 hrs									
95	Place Selected Candidate(s) in job	6 hrs	Tue 7/1/08	Wed 7/2/08	100%	6 hrs	92								
96	Search Results Page	4 hrs	Wed 7/2/08	Wed 7/2/08	100%	4 hrs	95								
97	Sort Functions	4 hrs	Wed 7/2/08	Thu 7/3/08	100%	4 hrs	96								
98	Filter Functions	4 hrs	Thu 7/3/08	Thu 7/3/08	100%	4 hrs	97								
99	Job Search Results	24 hrs	Thu 7/3/08	Tue 7/8/08	75%	24 hrs	98								
100	Video	39.75 days	Fri 5/9/08	Fri 7/4/08	100%	48 hrs									
101	Flash Media Server Implementation	2 days	Fri 5/9/08	Tue 5/13/08	100%	16 hrs									
102	Pay Per View	1 day	Tue 5/13/08	Wed 5/14/08	100%	8 hrs									
103	available credits	1 day	Tue 5/13/08	Wed 5/14/08	100%	8 hrs	101								
104	Access Rules	2 days	Wed 7/2/08	Fri 7/4/08	100%	16 hrs	113								
105	Buy and Implement Flash Player	1 day	Fri 5/16/08	Mon 5/19/08	100%	8 hrs									
106	Algorithms	51.25 days	Mon 4/14/08	Tue 6/24/08	100%	10 hrs									
107	Candidate to Job Match	0.75 days	Mon 6/23/08	Tue 6/24/08	100%	6 hrs									
108	% complete of profile	0.5 days	Mon 4/14/08	Mon 4/14/08	100%	4 hrs									
109	Company Pipeline	6 days	Tue 6/24/08	Wed 7/2/08	92%	48 hrs									
110	Build the Job Display Widget	1 day	Tue 6/24/08	Wed 6/25/08	100%	8 hrs	107								
111	Create Company Pipeline Results	2 days	Wed 6/25/08	Fri 6/27/08	100%	16 hrs	110								
112	Modify Company Talent Pipeline to Store Jobs for Candidates	2 days	Fri 6/27/08	Tue 7/1/08	100%	16 hrs	111								
113	Complete e-Commerce Integration	1 day	Tue 7/1/08	Wed 7/2/08	50%	8 hrs	112								
114	Candidate Profile Feedback-Code Revisions	11 days?	Mon 6/30/08	Mon 7/14/08	0%	0 hrs									
115	Provide User Case Revisions to GalvinTech	0 days	Mon 6/30/08	Mon 6/30/08	0%	0 hrs									
116	Provide Registration Wire Frame	0 days	Mon 6/30/08	Mon 6/30/08	100%	0 hrs									
117	Provide Candidate Profile Wire Frame	0 days	Mon 6/30/08	Mon 6/30/08	100%	0 hrs									
118	Provide Video from Kristian Andersen for Testing Video Iss	0 days	Mon 6/30/08	Mon 6/30/08	0%	0 hrs									
119	Provide Verbiage for Greeting	0 days	Mon 6/30/08	Mon 6/30/08	100%	0 hrs									
120	Provide values for Company & Industry Types	0 days	Mon 6/30/08	Mon 6/30/08	100%	0 hrs									
121	Apply Code Revisions to Activation Page	1 day?	Mon 6/30/08	Mon 6/30/08	100%	0 hrs									
122	Apply Code Revisions to General Fixes	1 day?	Tue 7/1/08	Tue 7/1/08	75%	0 hrs	121								
123	Apply Code Revisions to Registration	1 day?	Wed 7/2/08	Wed 7/2/08	75%	0 hrs	122								
124	Apply Code Revisions to Greeting	1 day?	Thu 7/3/08	Thu 7/3/08	100%	0 hrs	123								
125	Apply Code Revisions to Edit User Information	1 day?	Fri 7/4/08	Fri 7/4/08	75%	0 hrs	124								
126	Apply Code Revisions to Ideal Job Profile	1 day?	Mon 7/7/08	Mon 7/7/08	50%	0 hrs	125								
127	Apply Code Revisions to Job Preferences	1 day?	Tue 7/8/08	Tue 7/8/08	50%	0 hrs	126								
128	Apply Code Revisions to Work Experience	1 day?	Wed 7/9/08	Wed 7/9/08	100%	0 hrs	127								
129	Apply Code Revisions to Education	1 day?	Thu 7/10/08	Thu 7/10/08	100%	0 hrs	128								
130	Apply Code Revisions to Career Tracker	1 day?	Fri 7/11/08	Fri 7/11/08	50%	0 hrs	129								
131	Apply Code Revisions to Video Components	1 day?	Mon 7/14/08	Mon 7/14/08	100%	0 hrs	130								
132	Test & Implement	26 days	Tue 7/8/08	Wed 8/13/08	3%	328 hrs									
133	First Round System Testing	5 days	Tue 7/8/08	Tue 7/15/08	25%	40 hrs	104,99								
134	Second Round System Testing	5 days	Tue 7/15/08	Tue 7/22/08	0%	80 hrs	133								
135	User Acceptance Testing	5 days	Tue 7/22/08	Tue 7/29/08	0%	40 hrs	134								
136	Site Implementation & Validation	1 day	Tue 7/29/08	Wed 7/30/08	0%	8 hrs	135								
137	Initial Production Support	10 days	Wed 7/30/08	Wed 8/13/08	0%	160 hrs	136								

